



Update on Bicycle Master Plan Implementation Plan

Seattle Bicycle Advisory Board
Brian Macik and Wyatt Hoffman
February 1, 2017



Seattle
Department of
Transportation

Our mission, vision, and core values

Mission: deliver a high-quality transportation system for Seattle

Vision: connected people, places, and products

Committed to **5 core values** to create a city that is:

- Safe
- Interconnected
- Affordable
- Vibrant
- Innovative

For **all**

Presentation overview

- Objective
- 2016 Status Report
- Recap of Nov. 2016 meeting
- Updated project list
- Get input on 5-Year Plan draft document
- Next Steps

Objective

- Provide 2016 status report
- Provide update on status of 2017-2021 implementation plan
- Select “Strategies and Actions” for 2017-2021 implementation plan

2016 Status Report (1 of 2)

2016 BMP Projects	Completion Status	Estimated Completion	Notes
2 nd Ave PBL (Yesler Way to S Washington St)	Complete		
N 34 th St PBL	Complete		
Roosevelt Way NE PBL	Complete		
University Bridge PBL	Complete		
Westlake Ave N PBL	Complete		
Delridge Way SW PBL	Complete		
Meridian Ave N BL	Complete		
Renton Ave S BL	Complete		
SW Admiral Way BL	Complete		Additional ped improvements expected in 2017
Wedgewood NGW	Complete		
Central E-W NGW	Complete		Interim is complete, final to be constructed in 2017
5 th Ave Sharrow	Complete		

2016 Status Report (2 of 2)

2016 BMP Projects	Completion Status	Estimated Completion	Notes
Banner Way NE BL		2017	Waiting for good weather/Sound Transit
Dexter Ave N PBL		2017	Waiting for good weather
N 92d St PBL		2017	Waiting for good weather
Gilman Ave W PBL		2017	Added to contract with Nickerson St paving
S Dearborn St PBL		2017	Requires WSDOT approval and phasing coordination with paving project
9 th Ave N PBL		2017, 2018	Private construction and utility issues 2017 – Westlake Ave N to Harrison St 2018 – Harrison St to Denny Way
SODO Trail		2018-2019	ROW ownership issues


Recap of Nov. 2016 Meeting

- 2017-2021 Project List
 - SBAB-identified preferred projects (Tier 1)
 - Partner projects (paving, transit, etc.)
- SDOT took input from the three sector groups (North, Central, South)
 - Reps. brought input from those who couldn't attend
- SDOT presented draft list at Nov. SBAB meeting
 - Prioritized projects, final decisions made
- Current proposed 2017-2021 mileage: 69 miles
- Opportunities for adding/changing/removing 2020 and 2021 projects will be available next year in 2018-2022 plan


Project List

- 5-year network provides all ages and abilities connections
- Changes to list since November:
 - Added 4th Ave Phase I (2017) and Phase II (2018) (BL, 0.28/0.69 mi)
 - Added Roy St/Valley St to 2021 (PBL, 0.25 mi)
 - Deleted W Nickerson St 2018 Paving Project (BL, 0.43 mi)


2017-2021 Projects (1 of 3)

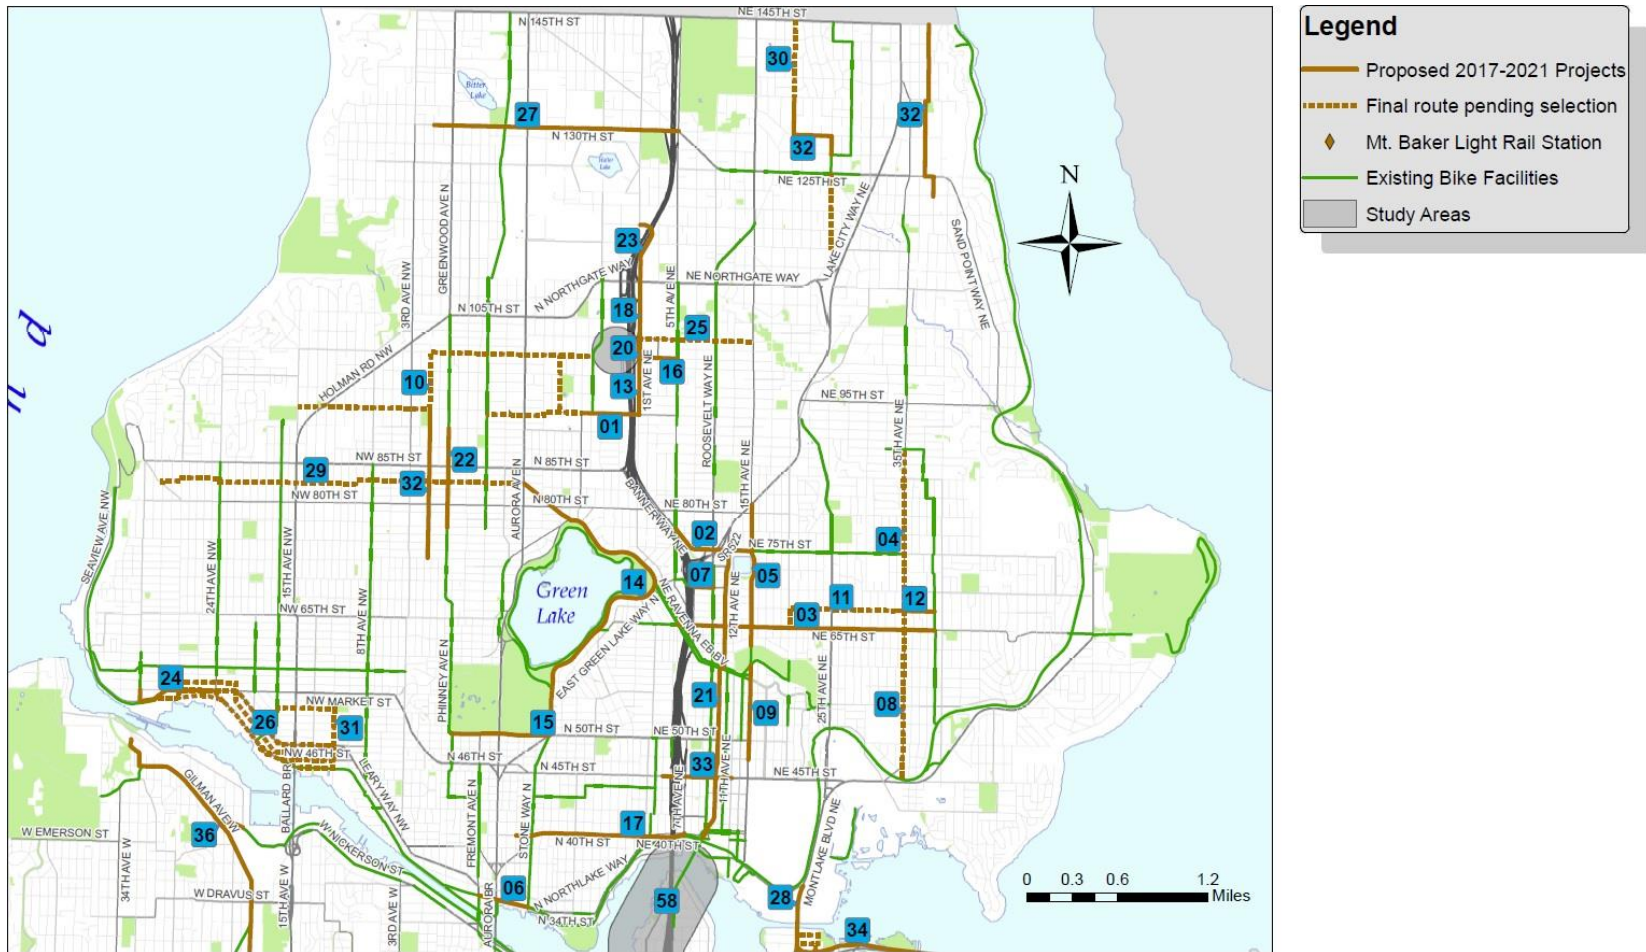

2017-2021 Projects (2 of 3)

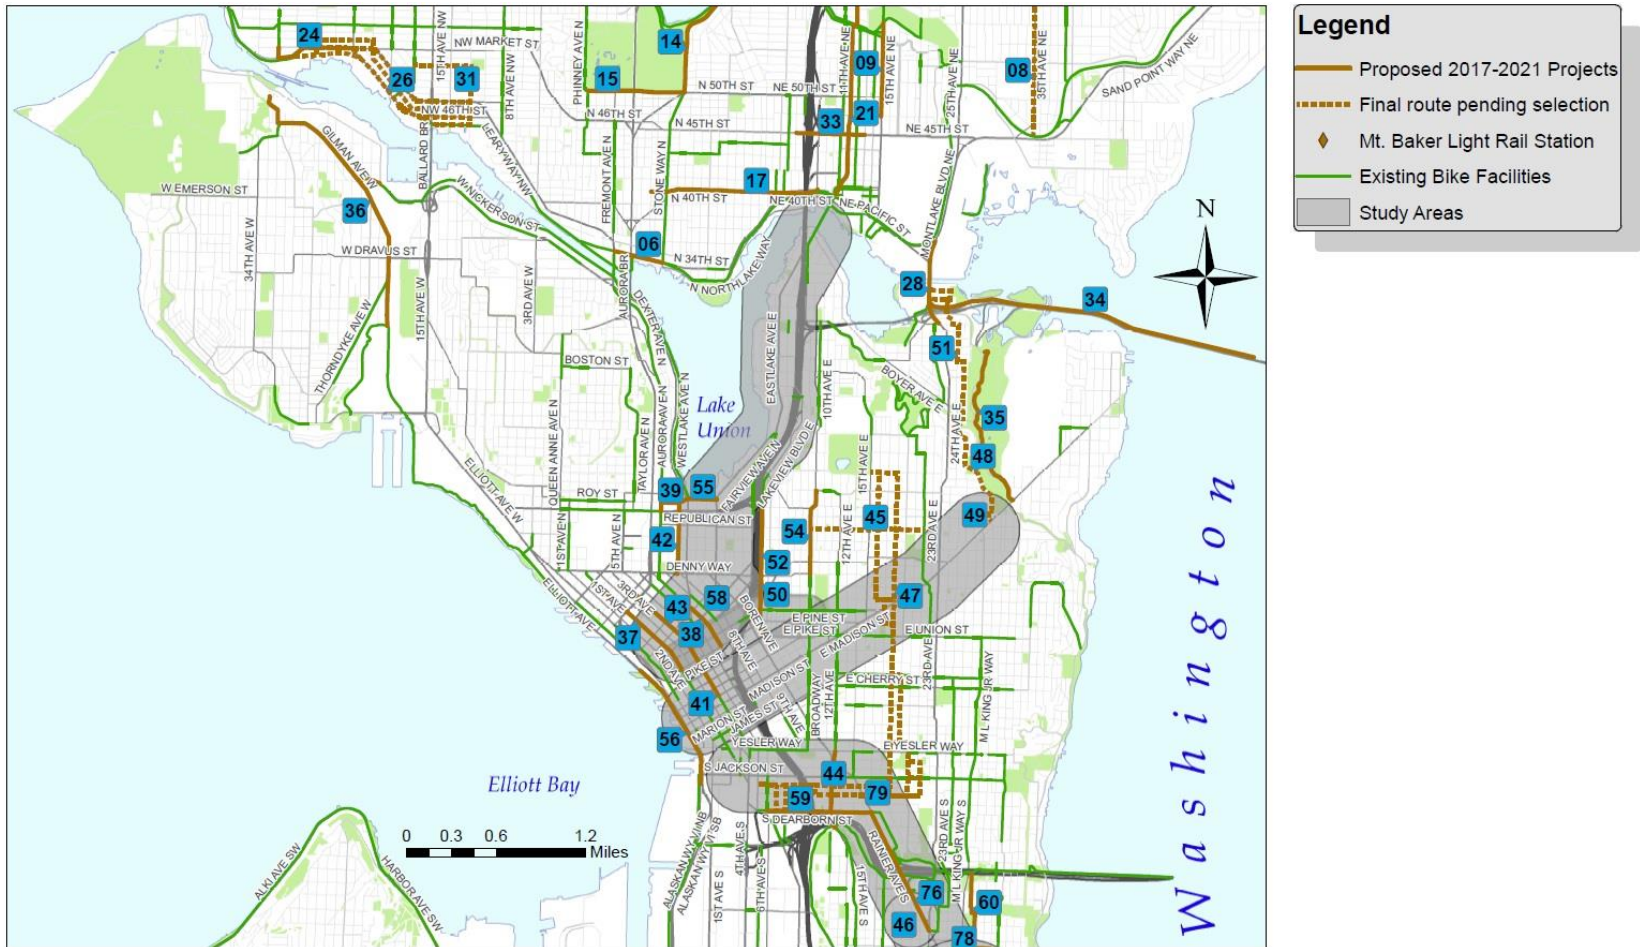

2017-2021 Projects (3 of 3)

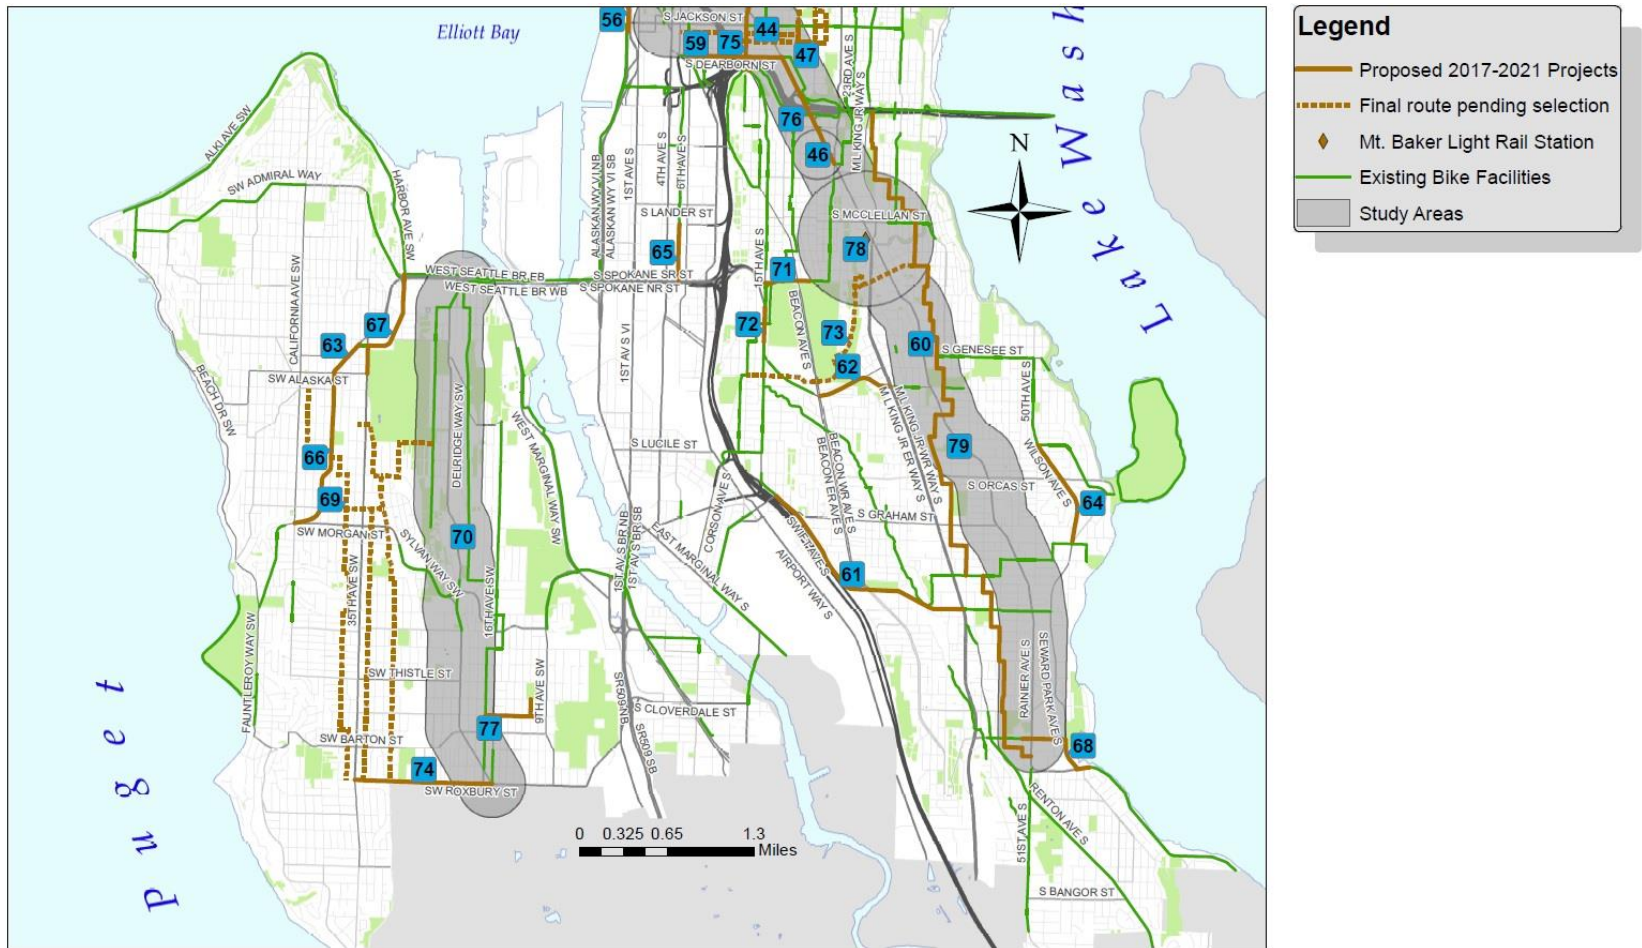

Draft Document

- Simplified
- Reduced repetition of BMP
- Added section on “BMP Progress”
- Improved clarity and prominence of project list and maps
- Added “Budget” section
- Need input on “Strategies and Actions” section



Next steps

Date	Activity/action
Feb. 1 st	SBAB Update [we're here]
Late Feb.	Finalize document and provide draft to City Council and SBAB
March	Submit final to City Council

Questions?

Brian.Macik@seattle.gov

Monica.DeWald@seattle.gov

<http://www.seattle.gov/transportation/bikemaster.htm>



Seattle
Department of
Transportation
